


Vacuum Chamber Centerline Profile to Magnetic Axis X Centerline, Green line = +/- .100 Tol.

Red = Actual Chamber Centerline

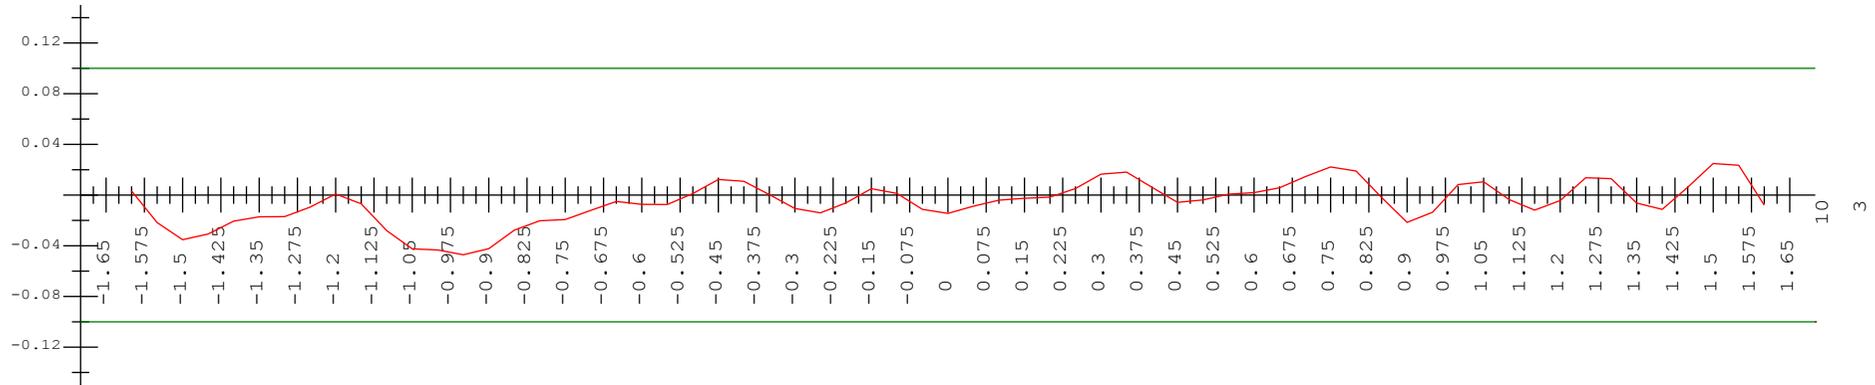

Quadrupole

Value	Nominal	Actual	Deviation
X Center	0.000	0.033	0.033
Y Center	0.000	-0.028	-0.028
Z Center	1830.000	1829.949	-0.051
Roll	0.000	0.184	0.184
Pitch	0.000	0.433	0.433
Yaw	0.000	-0.436	-0.436

BPM

Value	Nominal	Actual	Deviation
US X	0.000	0.016	0.016
US Y	0.000	0.032	0.032
DS X	0.000	0.014	0.014
DS Y	0.000	0.004	0.004
Roll	0.000	0.399	0.399
BPM-QUAD	128.120	128.142	0.022

Phase Shifter Chamber

Value	Nominal	Actual	Deviation
US X	0.000	-0.130	-0.130
US Y	0.000	-0.084	-0.084
DS X	0.000	-0.177	-0.177
DS Y	0.000	0.055	0.055

Dimensions in MM, Angles in Milliradians



HGVPU -

Chamber Profile and Interspace Components

Installed Quad S/N: 0746

S/N : HXU_027
Date : 15-NOV-2019
Data Set : 0001
Run : RUN 1
Cam Pos. : B
