



MFD NON-COMPLIANCE REPORT # 30121-1


PART NAME: **HXU PROTO INTERSPACE PL**
PF/SA NO.: **SA-389-893-00 R1**
WORK ORDER NO.: **30121-1 (8924593)**
VENDOR **MFD**

DATE: **6/17/13**
INSPECTOR: **K. CABAN**
ENGINEER: **D. BRUCH** EXT.:
ROUTE TO: **OV PLATE**

Reason For Non-Compliance:

Action (UAI,RWK,SCRP)

1. Distance of Helicoil $\frac{1}{2}$ -13 (STI Thread) 2X 36.500 \pm 0.005" is out of tolerance on 1 of 2 holes measuring 36.4906 (-0.0044" out of tolerance). See below for location and for clarity.

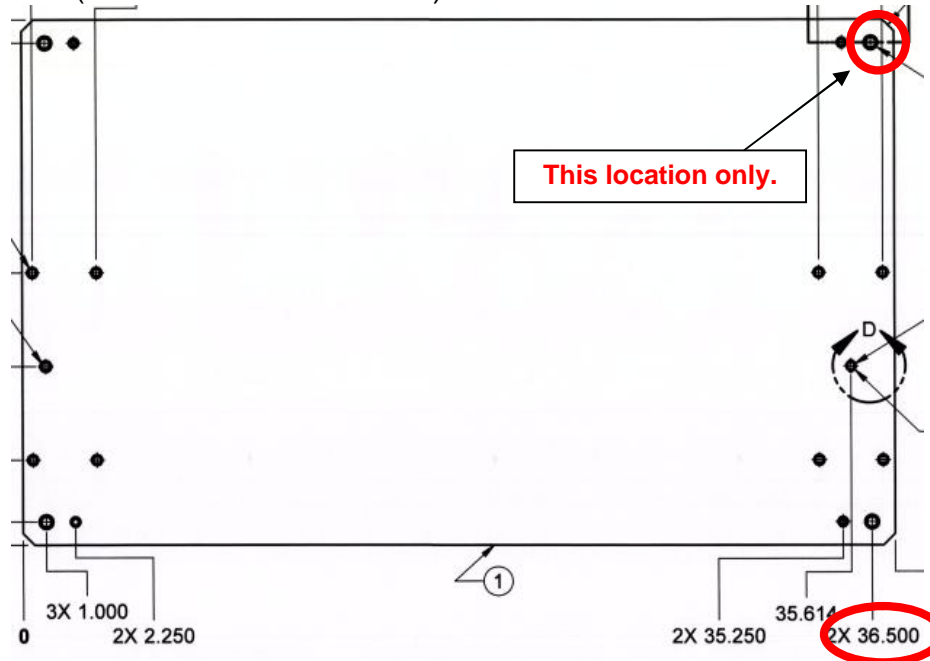

2. With respect to the Waterjet cut, holes near end of length drifted X = -0.009", Y = -0.008".

Engineer Signature: _____ Date: _____
